



Classroom Building at Charlottetowne & 5th

Central Campus

Weekly Update October 11, 2019

CREECH & ASSOCIATES



Meetings & Milestones

- **This Week:**

- Continue Level 4 Overhead MEP Rough-In
- Continue Level 3 Fire protection System
- Complete Level 3 In-Wall Plumbing Rough-In
- Continue Level 4 In-Wall Electrical Rough-In
- Continue Level 3 In-Wall Electrical Rough-In
- Complete Penthouse Electrical Rough-In
- Continue Installing Mechanical Pumps
- Continue Insulating Exterior Walls
- Begin Hanging Level 4 Drywall
- Begin Hanging Penthouse Drywall
- Continue Installing Blocking
- Continue Installing Brick Ties
- Continue Installing Plan West Brick and Cast Stone
- Continue Installing Plan North Cast Stone Watertable
- Install Plan North Elevation Spray Foam
- Complete Installing Additional Fireproofing at Shaft Support Steel

Meetings & Milestones

• **Next Week:**

- Continue Level 3 Overhead MEP Rough-In
- Continue Level 3 Fire protection System
- Continue Level 2 In-Wall Plumbing Rough-In
- Complete Level 4 In-Wall Electrical Rough-In
- Continue Level 3 In-Wall Electrical Rough-In
- Continue Installing Mechanical Pumps
- Continue Insulating Exterior Walls
- Continue Hanging Penthouse Drywall
- Continue Hanging Level 4 Drywall
- Continue Installing Blocking
- Continue Installing Brick Ties
- Continue Installing Plan West Brick and Cast Stone
- Continue Installing Plan North Cast Stone Watertable



CENTRAL PIEDMONT
COMMUNITY COLLEGE

RODGERS

Our Passion is Building®

Progress Photos



**Continue Installing
Mechanical Pumps
in Mech Room 193**



Progress Photos



**Continue level 3
Sprinkler System**



Progress Photos



**Continue Level 3
Overhead Plumbing
Rough-In**





Progress Photos



**Continue Level 3
In-Wall Plumbing
Rough-In**





Progress Photos



**Continue Level 3
In-Wall Electrical
Rough-In**



Progress Photos



**Continue Installing
AV Boxes**






CENTRAL PIEDMONT
COMMUNITY COLLEGE

RODGERS

Our Passion is Building®

Progress Photos

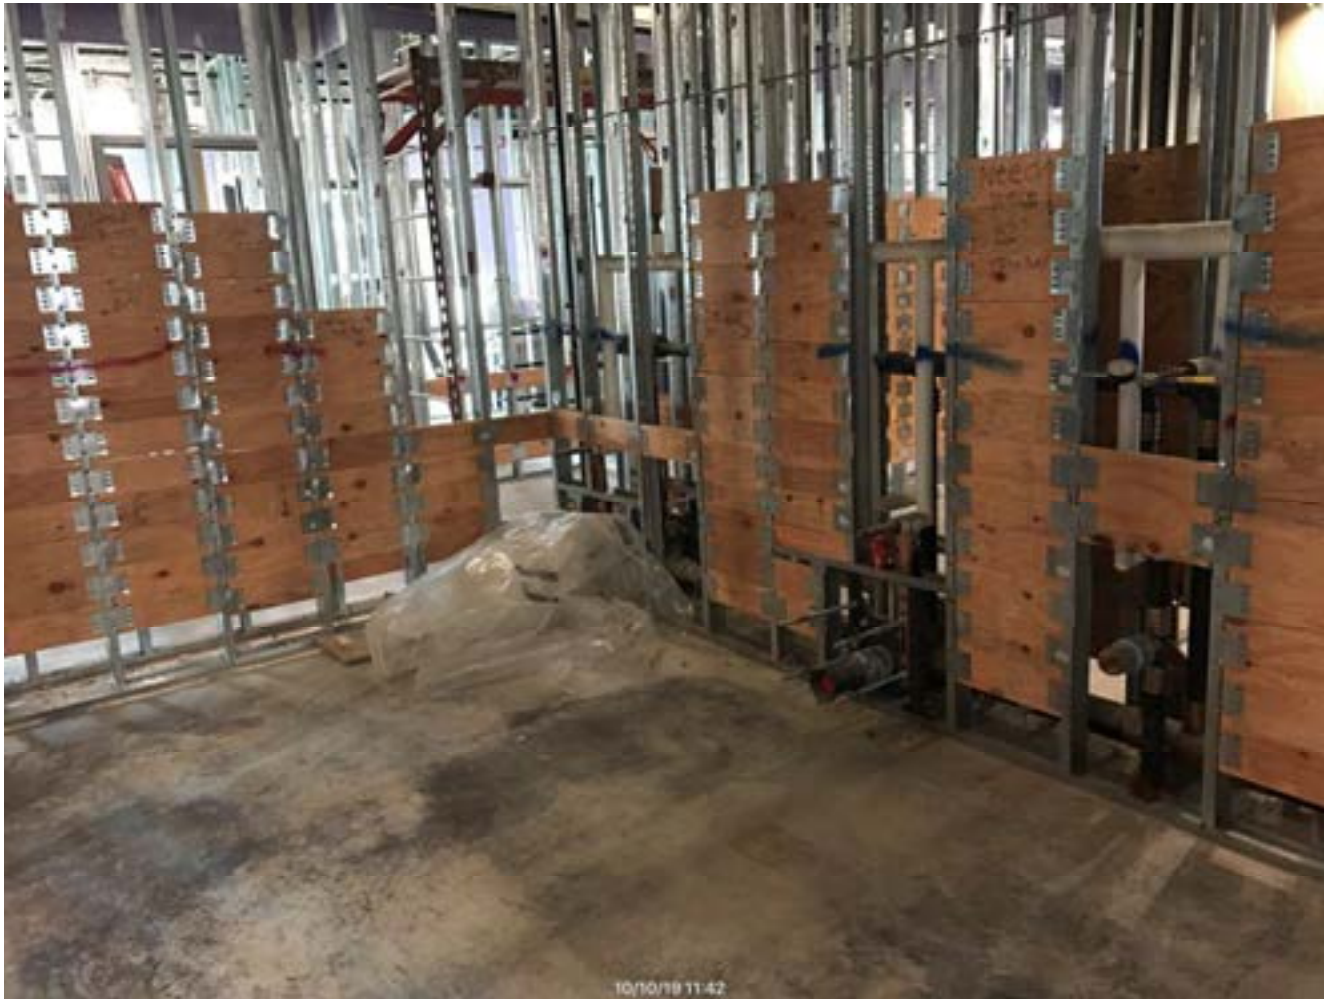

**Continue Installing
Blocking**





Progress Photos



**Continue Installing
Blocking at Stair 3**



Progress Photos



**Begin Hanging
Drywall at Stair 1**



Progress Photos



**Continue Insulating
Level 4 Exterior
Walls**





CENTRAL PIEDMONT
COMMUNITY COLLEGE

RODGERS

Our Passion is Building®

Progress Photos



Begin Hanging Fourth Floor Exterior Drywall



Progress Photos



**Begin Hanging
Penthouse Drywall**



Progress Photos



**Continue Plan North
Spray Foam**



Progress Photos



**Continue Installing
Brick Ties on the
Plan South Elevation**





CENTRAL PIEDMONT
COMMUNITY COLLEGE

RODGERS

Our Passion is Building®

Progress Photos



**Continue Plan West
Brick and Cast Stone**



Conclusion of Weekly Update 10/11/2019

Our
Passion
is Building®

