



# Merancas Classroom Building

Merancas Campus

Weekly Update November 15, 2019



## Meetings & Milestones

- **This Week:**

- Continue Installing Fluid Applied Air Barrier System
- Continue Installing Level 3 Interior Framing
- Continue Installing Door Frames
- Continue Installing Brick Ties and Flashing
- Begin Installing Temporary Windows
- Continue Area A and B Roofing System
- Begin HVAC 4-Pipe System
- Complete First Floor Ductwork and VAV Rough-In
- Continue Second Floor Ductwork
- Continue Second and Third Floor HVAC Piping Rough-In
- Continue First and Second Floor Electrical Rough-In
- Begin First Floor Plumbing Insulation
- Complete First Floor Plumbing Rough-In
- Continue Second Floor Plumbing Rough-In
- Continue Second Floor Fire Protection System
- Begin Third Floor Fire Protection System
- Continue Installing Elevator Tube Steel

## Meetings & Milestones

- **Next Week:**

- Continue Installing Fluid Applied Air Barrier System
- Continue Installing Level 3 Interior Framing
- Continue Installing Door Frames
- Continue Installing Brick Ties and Flashing
- Begin South Elevation Spray Foam
- Continue Installing Temporary Windows
- Continue Area A and B Roofing System
- Continue HVAC 4-Pipe System
- Continue Second Floor Ductwork
- Continue Second and Third Floor HVAC Piping Rough-In
- Continue First and Second Floor Electrical Rough-In
- Continue First Floor Plumbing Insulation
- Continue Second Floor Plumbing Rough-In
- Continue Second Floor Fire Protection System
- Continue Third Floor Fire Protection System
- Continue Installing Elevator Tube Steel

Progress Photos



**Complete First Floor  
In-Wall Plumbing  
Rough-In**






Progress Photos



**Begin First Floor  
Plumbing Insulation**



Progress Photos




**Continue First Floor  
In-Wall Electrical  
Rough-In**






Progress Photos



**Continue Second  
Floor In-Wall  
Plumbing Rough-In**



Progress Photos



**Continue Second  
Floor In-Wall  
Electrical Rough-In**





Progress Photos



**Continue Second  
Floor Mechanical  
Piping**



Progress Photos



**Continue Second  
Floor Overhead MEP  
Rough-In**





Progress Photos



**Begin Third Floor  
Sprinkler System**





Progress Photos



**Continue Third Floor  
Mechanical Piping**



Progress Photos



**Continue Elevator  
Tube Steel**





Progress Photos



**Continue First Floor  
Blocking**






Progress Photos



**Continue Third Floor  
Interior Framing**

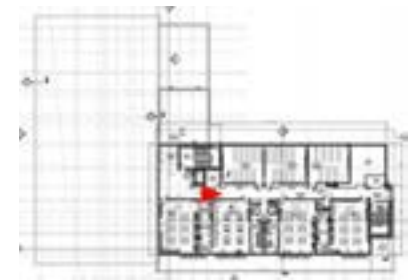

Progress Photos



**Begin Excavating for  
Underground HVAC  
Piping System**



## Progress Photos



**Continue Area A  
Roofing System**





Progress Photos



**Continue Brick Ties  
and Flashing**



## Progress Photos



**Begin Installing  
Temporary Windows**



Conclusion of Weekly Update 11/15/2019

Our  
Passion<sup>®</sup>  
is Building<sup>®</sup>

