



# Classroom Building at Charlottetowne & 5th

Central Campus

Weekly Update January 17, 2020

CREECH & ASSOCIATES



## Meetings & Milestones

- **This Week:**

- Continue Penthouse Ductwork
- Continue Data Cabling
- Continue Installing Fourth Floor Electrical Devices
- Continue Installing Third Floor Electrical Devices
- Continue Insulating First Floor Interior Walls
- Continue Hanging First Floor Interior Walls
- Continue Taping and Finishing First Floor Interior Walls
- Continue Second Floor Primer
- Begin First Floor Primer
- Install Fourth and Third Floor Window Sills
- Begin Installing Fourth Floor Ceiling Tile
- Continue Installing Second Floor Ceiling Grid
- Continue Installing Third Floor Ceiling Grid
- Continue Installing Third Floor Light Fixtures
- Continue Plan East Masonry and Cast Stone
- Continue Plan North Masonry and Cast Stone
- Continue Plan South Masonry and Cast Stone

## Meetings & Milestones

- **Next Week:**
  - Continue Penthouse Ductwork
  - Continue Data Cabling
  - Continue Installing Fourth Floor Electrical Devices
  - Continue Installing Third Floor Electrical Devices
  - Continue Insulating First Floor Interior Walls
  - Continue Hanging First Floor Interior Walls
  - Continue Taping and Finishing First Floor Interior Walls
  - Continue Second Floor Primer
  - Continue First Floor Primer
  - Continue Installing Second Floor Ceiling Grid
  - Continue Installing Third Floor Ceiling Grid
  - Continue Installing Third Floor Light Fixtures
  - Continue Installing Fourth Floor Ceiling Tile
  - Continue Plan East Masonry and Cast Stone
  - Continue Plan North Masonry and Cast Stone
  - Continue Plan West Masonry and Cast Stone
  - Continue Plan South Masonry and Cast Stone
  - Begin Fourth Floor Flooring
  - Begin Fourth Floor Casework

Progress Photos



**Continue Hanging  
Main Lobby Drywall**



**Location: Lobby 171**

Progress Photos



**Continue Taping  
Stair 2 Drywall**



**Location: Stair 2**

Progress Photos



**Begin Priming First  
Floor Drywall**



**Location: Corridor 176**

Progress Photos



**Continue Priming  
Second Floor Walls**



**Location: CADD Classroom 228**

Progress Photos



**Continue Installing  
Second Floor Ceiling  
Grid**



**Location: Classroom 200**



Progress Photos



**Begin Installing  
Second Floor  
Bathroom Tile**



**Location: Mens 280**

Progress Photos



**Begin Installing  
Second Floor  
Plumbing Fixtures**



**Location: Womens 281**

Progress Photos



**Continue Installing  
Third Floor Light  
Fixtures**



**Location: DMS 320**

Progress Photos




**Begin Installing  
Third Floor Window  
Sills**



**Location: Corridor 376**

Progress Photos

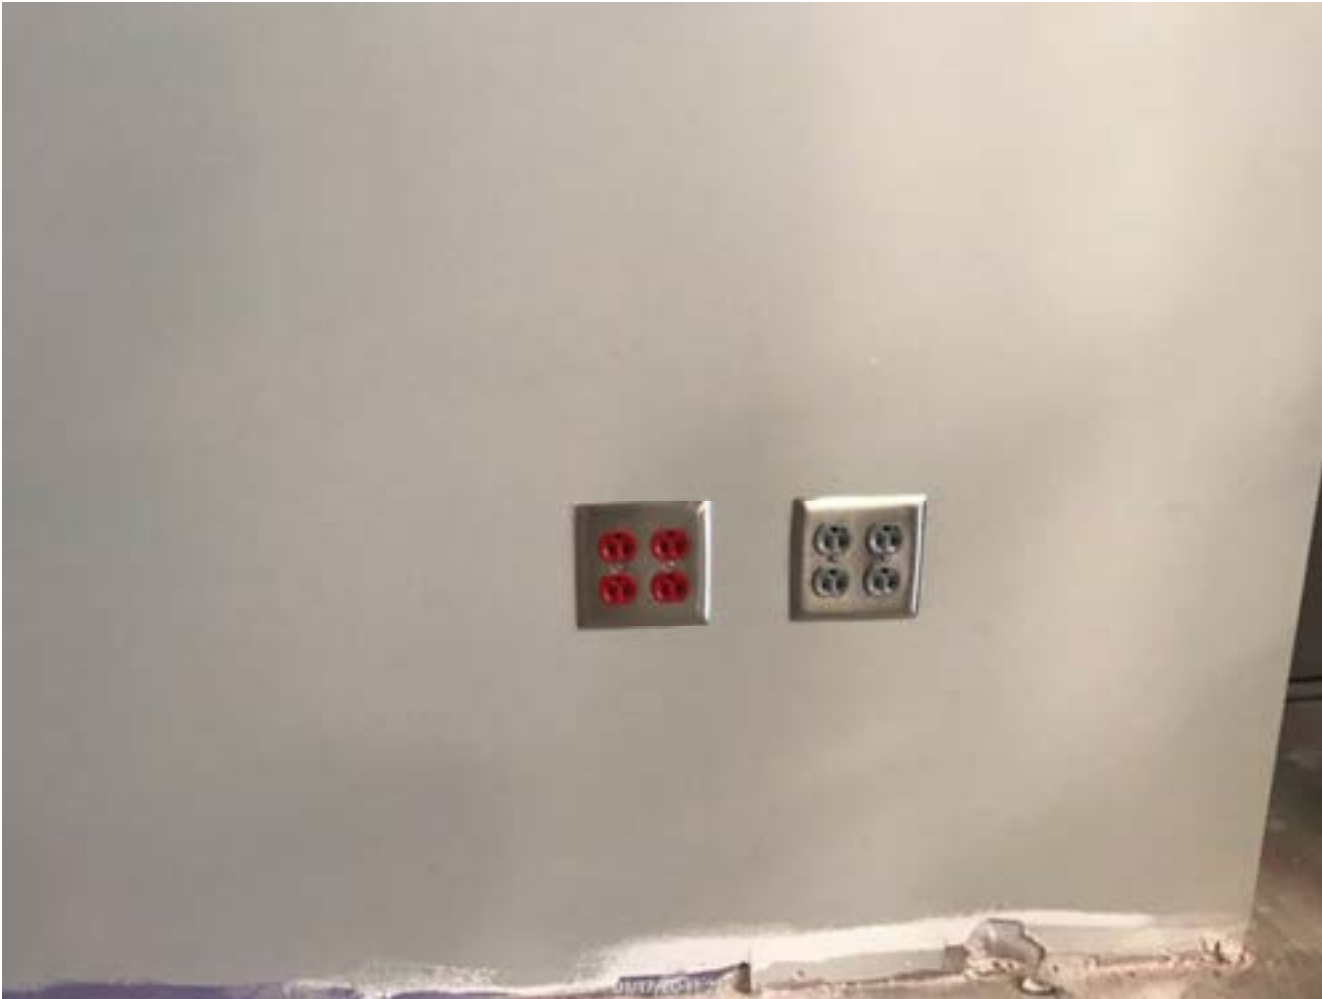

**Continue North  
Elevation Masonry  
and Cast Stone**



**Location: OR 438**

Progress Photos



**Install Fourth Floor  
Window Sills**



**Location: Mother Child Sim 444**

Progress Photos



**Begin Installing  
Fourth Floor Ceiling  
Tile**



**Location: Corridor 470**

Progress Photos



**Install Fourth Floor  
Home Suite Fan**




**Location: Bedroom 416**



Progress Photos



**Continue AHU  
Mechanical Piping**

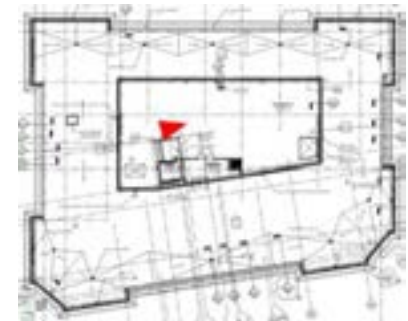

**Location: Mechanical 500**

Progress Photos



**Continue North  
Elevation Masonry  
and Cast Stone**



**Location: North Elevation**

Progress Photos



**Continue South  
Elevation Masonry  
and Cast Stone**



**Location: South Elevation**

Progress Photos



**Continue East  
Elevation Masonry  
and Cast Stone**



**Location: East Elevation**

Progress Photos



**Continue East  
Entrance Cast Stone**



**Location: East Elevation**

Conclusion of Weekly Update 01/17/2020

Our  
Passion  
is Building®

