



# Merancas Classroom Building

Merancas Campus

Weekly Update April 24, 2020



## Meetings & Milestones

### • **This Week:**

- Continue First and Second Floor Electrical Rough-In
- Continue Second Floor Ceiling Grid
- Continue Second Floor Data Cabling
- Complete Second Floor Restroom Tile
- Continue Second Floor Ductwork
- Continue Installing Interior Storefront
- Begin Installing Storefront Doors
- Continue Third Floor Ductwork
- Begin Third Floor Restroom Tile
- Prime Third Floor Drywall
- Continue Generator Enclosure Masonry
- Complete Seatwall Concrete Masonry

## Meetings & Milestones

### • **Next Week:**

- Continue First, Second and Third Floor Electrical Rough-In
- Begin Installing Restroom Plumbing Fixtures
- Continue Second Floor Ceiling Grid
- Continue Second Floor Data Cabling
- Continue Second Floor Ductwork
- Continue Installing Interior Storefront Frames
- Begin Installing Storefront Glass
- Continue Third Floor Ductwork
- Complete Third Floor Restroom Tile
- Prime Third Floor Drywall
- Continue Bick Cleaning
- Continue Masonry Joint Caulking

Progress Photos




**Continue Electrical  
Rough-In**



**Location: Electrical 169**

Progress Photos

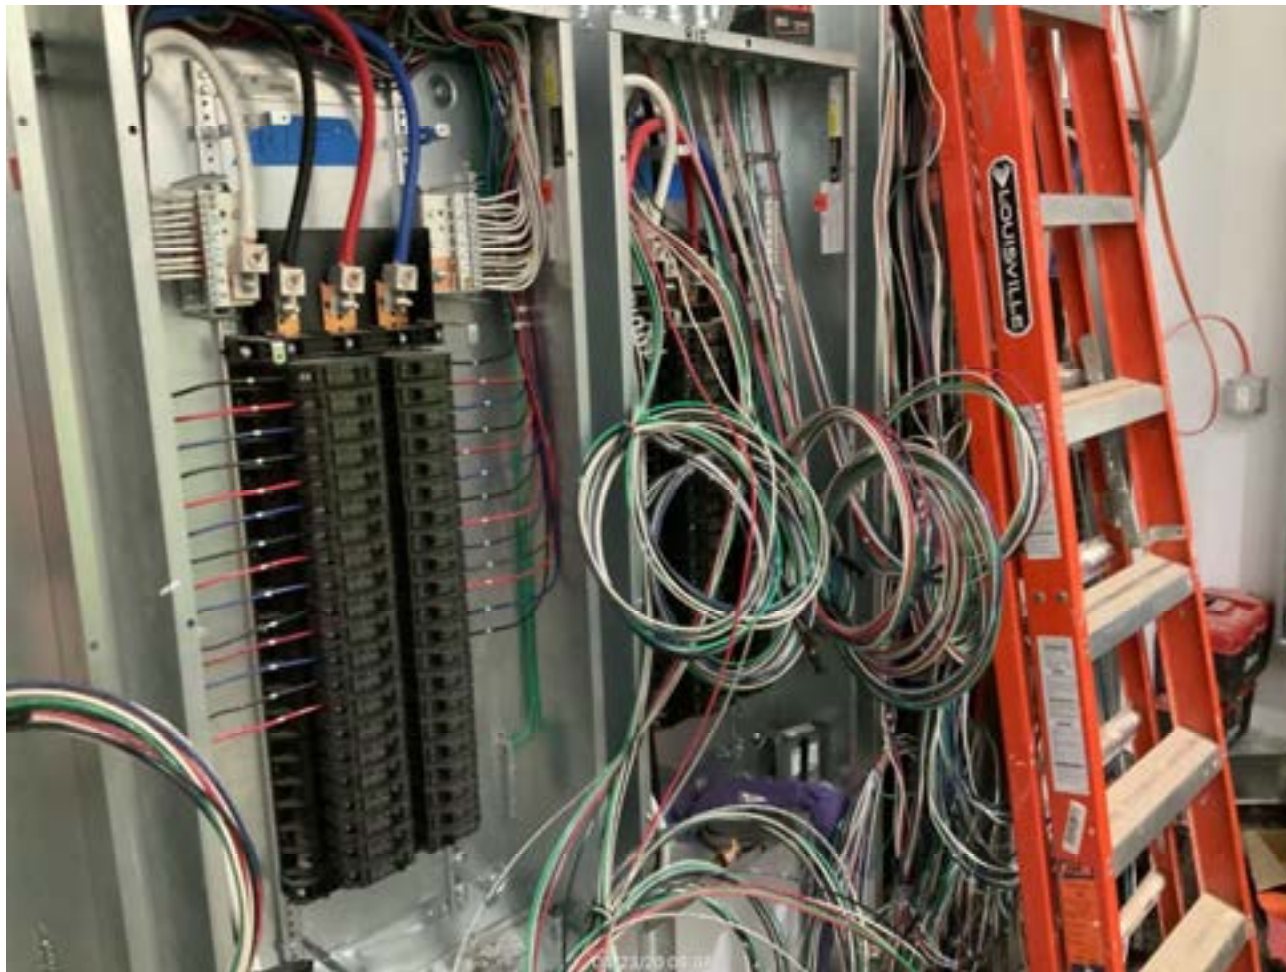

**Continue Pulling  
Electrical Room Wire**



**Location: Storage 113**

Progress Photos



**Continue Library  
Ductwork**



**Location: Library 122**

Progress Photos



**Continue Commons  
Area Ductwork**



**Location: Commons 142**

Progress Photos



**Continue Installing  
Interior Storefront**



**Location: Study 125**



Progress Photos



**Begin Installing  
Interior Storefront  
Doors**



**Location: Lobby 101**

Progress Photos



**Continue Second  
Floor Electrical  
Rough-In**



**Location: Electrical 234**

Progress Photos



**Continue Stairwell  
Drywall**



**Location: Stair 1**

Progress Photos



**Begin Third Floor  
Restroom Tile**



**Location: Men 320**

Progress Photos



**Install Exterior  
Storefront Doors**




**Location: South Elevation**

Progress Photos



**Continue Canopy  
Soffit Framing**

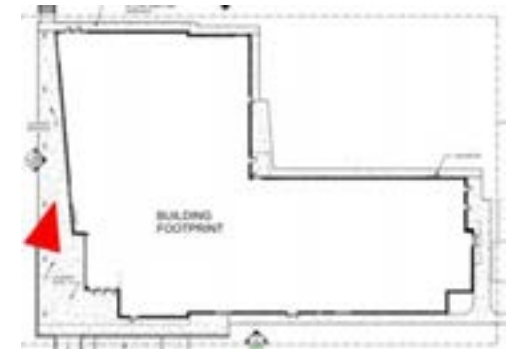

**Location: West Elevation**

Progress Photos



**Complete Seat Wall  
Masonry and Cast  
Stone**



**Location: Plan East**

## Progress Photos



**Continue Dumpster  
Enclosure Masonry**



**Location: Dumpster Enclosure**



Progress Photos



**Continue Grading  
Alternate Parking Lot**



**Location: Parking Lot**

Conclusion of Weekly Update 04/24/2020

Our  
Passion<sup>®</sup>  
is Building<sup>®</sup>

